







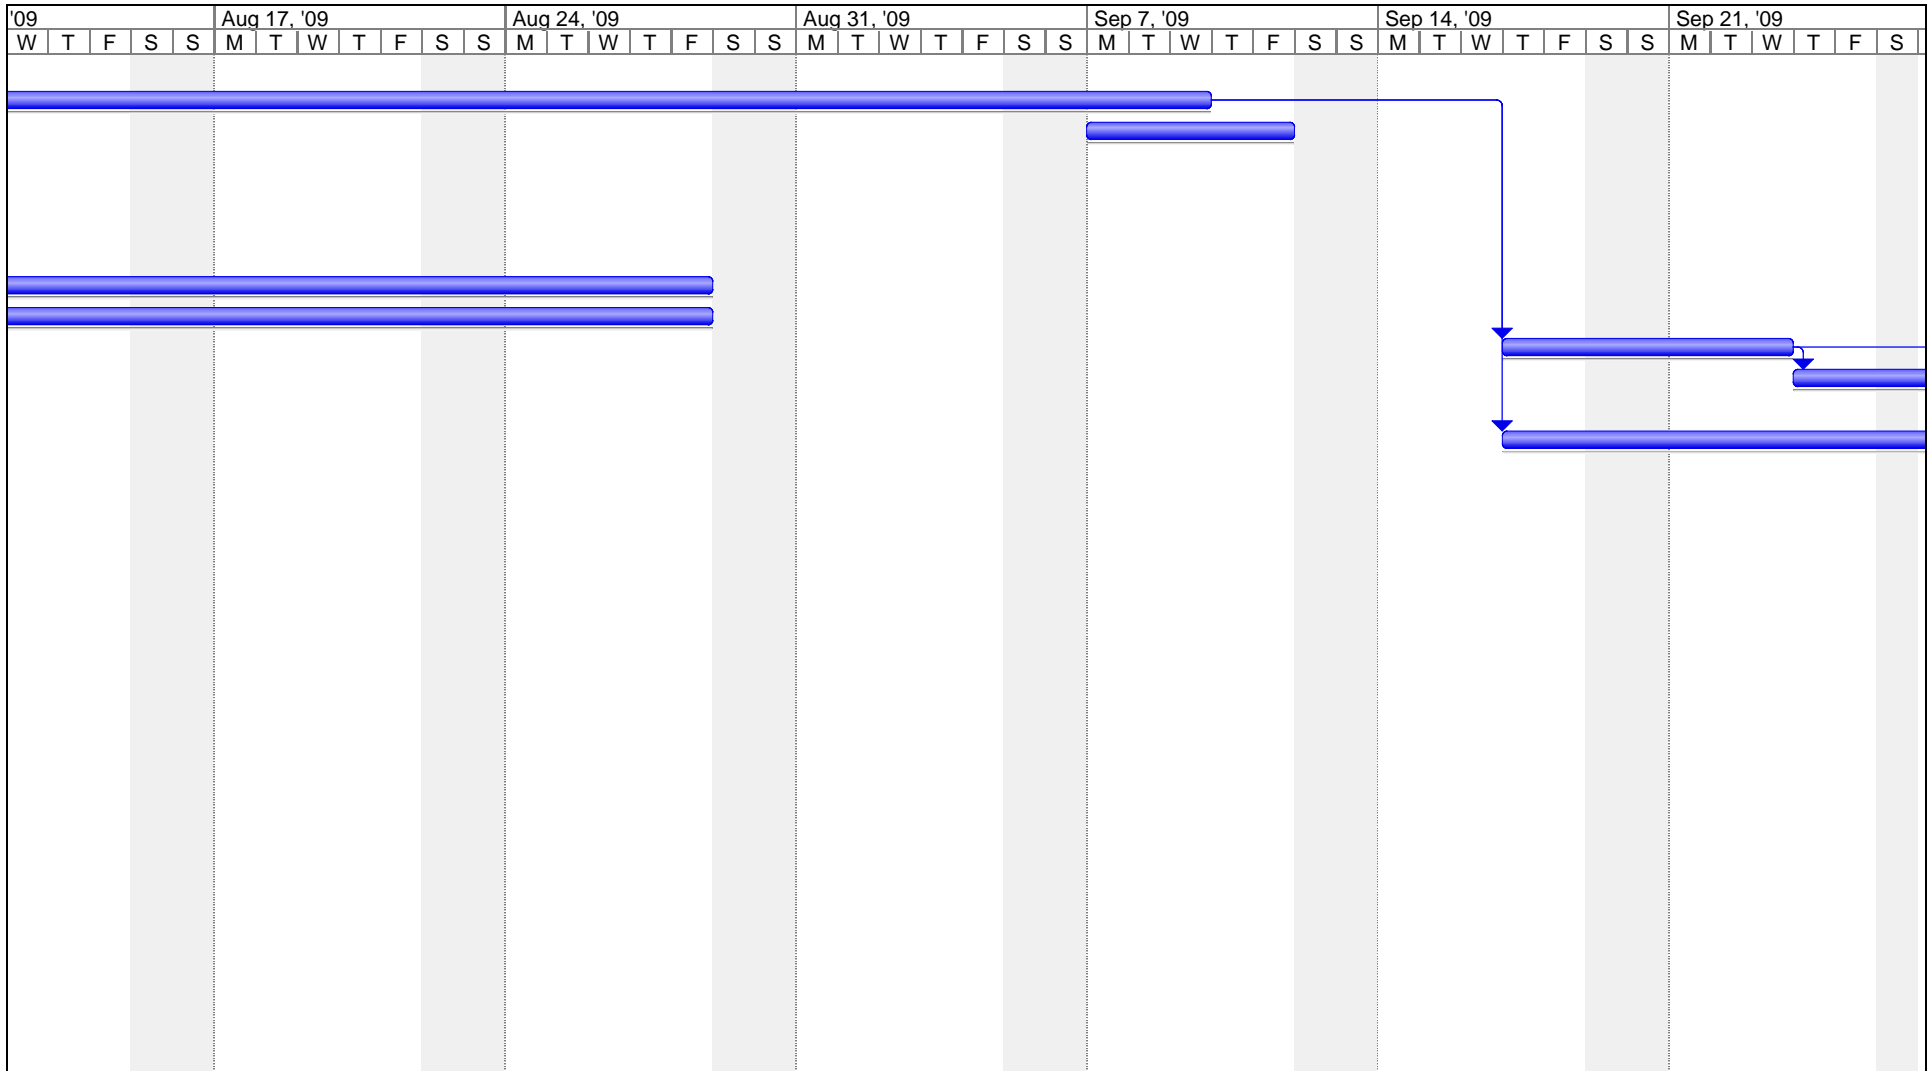

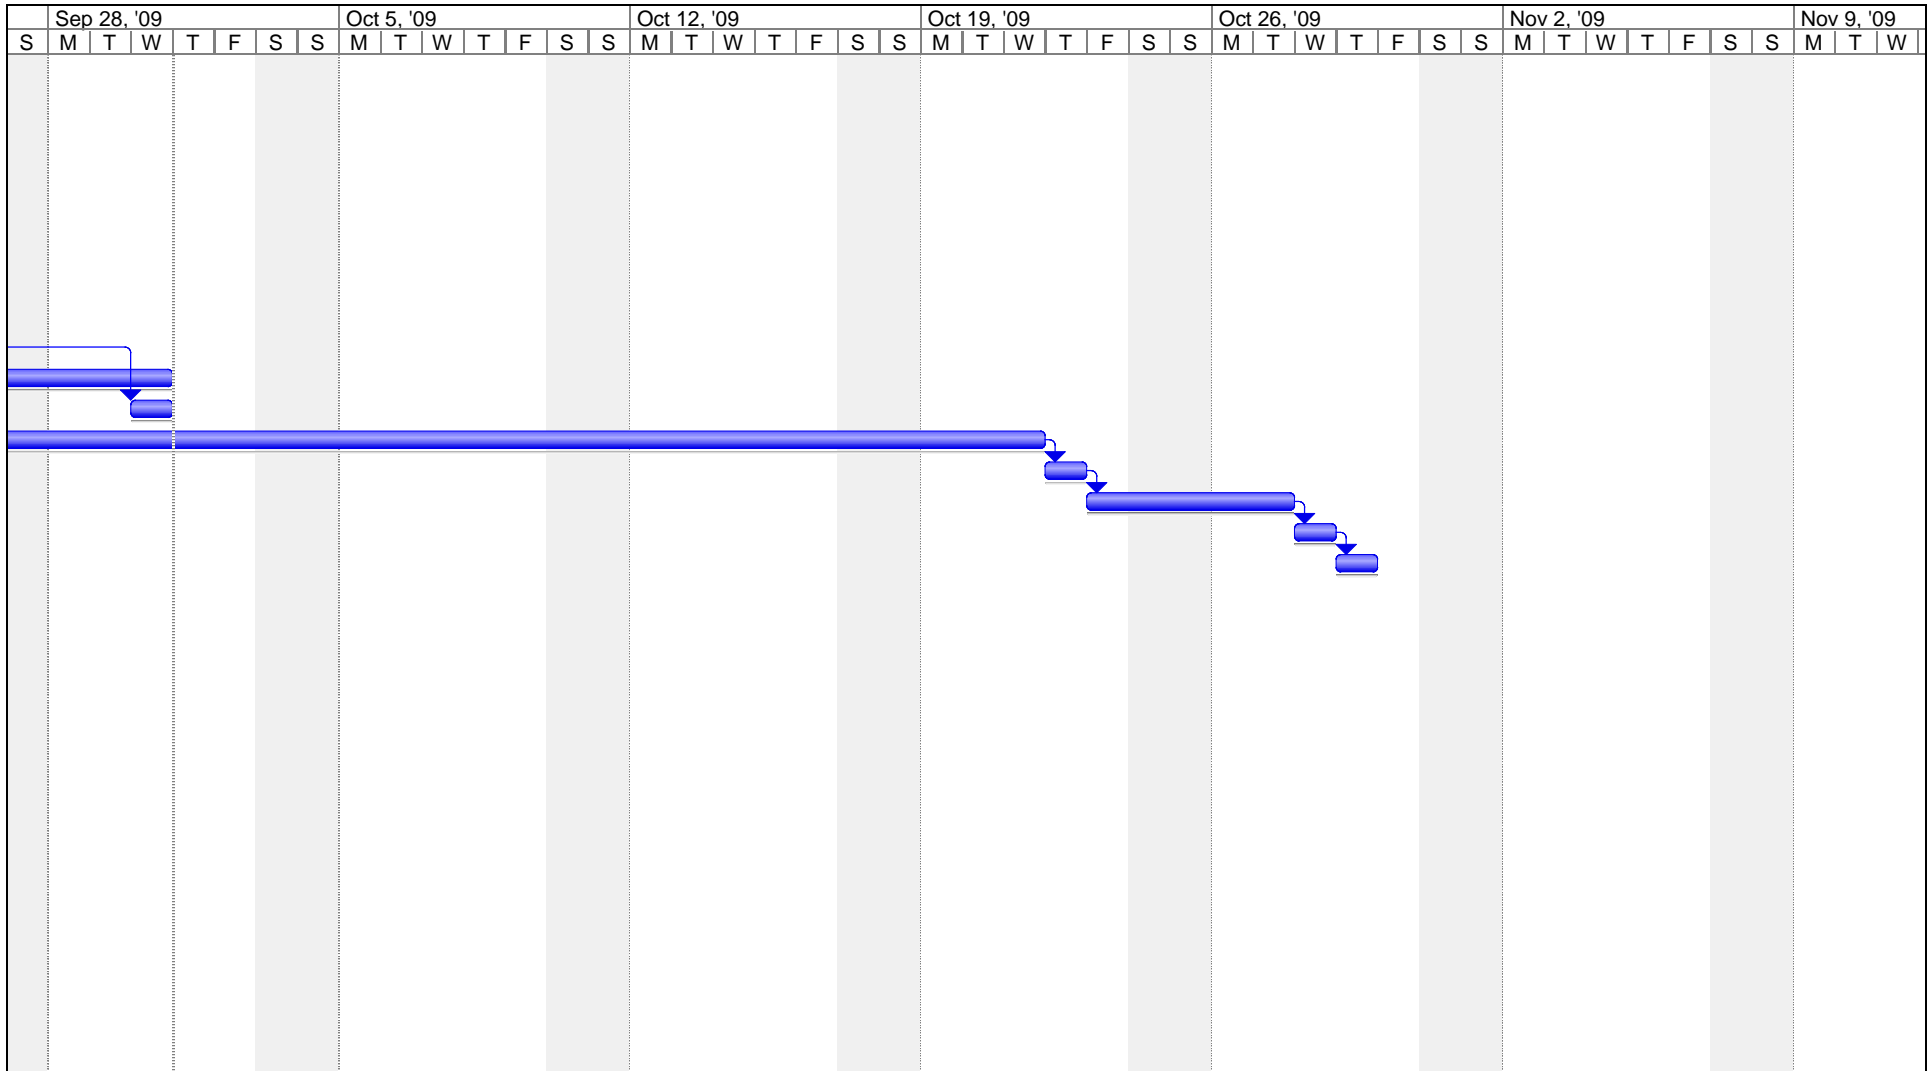


ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	7, '09							Aug 3, '09							Aug 10, '0		
							T	W	T	F	S	S	M	T	W	T	F	S	S	M	T		
1	DSA Approval	1 day	Thu 7/30/09	Thu 7/30/09																			
2	DSA Drawings Available	27 days	Tue 8/4/09	Wed 9/9/09	1																		
3	Front End Specs	5 days	Mon 9/7/09	Fri 9/11/09																			
4	Removal of Fire Alarm	2 days	Tue 8/4/09	Wed 8/5/09																			
5	Removal of Sprinkler Clock	1 day	Fri 8/7/09	Fri 8/7/09																			
6	Removal of AC Controls & Fibe	2 days	Mon 8/10/09	Tue 8/11/09																			
7	Demo Walk-through	1 day	Mon 8/10/09	Mon 8/10/09																			
8	Demolition	15 days	Mon 8/10/09	Fri 8/28/09																			
9	Air Quality Control	15 days	Mon 8/10/09	Fri 8/28/09																			
10	Advertisement #1	5 days	Thu 9/17/09	Wed 9/23/09	2																		
11	Advertisement #2	5 days	Thu 9/24/09	Wed 9/30/09	10																		
12	Job Walk	1 day	Wed 9/30/09	Wed 9/30/09	10																		
13	Bidding Period	25 days	Thu 9/17/09	Wed 10/21/09	2																		
14	Bid Opening	1 day	Thu 10/22/09	Thu 10/22/09	13																		
15	Bid Protest	3 days	Fri 10/23/09	Tue 10/27/09	14																		
16	Send Elaine Lowest Bid	1 day	Wed 10/28/09	Wed 10/28/09	15																		
17	Submit for Board Calendar	1 day	Thu 10/29/09	Thu 10/29/09	16																		
18	Board Meeting	1 day	Fri 11/13/09	Fri 11/13/09																			
19	Notice of Award	1 day	Mon 11/16/09	Mon 11/16/09	18																		
20	Pre Construction Meeting	1 day	Tue 11/17/09	Tue 11/17/09	19																		
21	Notice to Proceed	4 days	Tue 11/17/09	Fri 11/20/09	19																		
22	Construction	175 days	Mon 11/23/09	Fri 7/23/10	21																		
23	Punch List	5 days	Mon 7/12/10	Fri 7/16/10																			
24	FFE Programming & Selection	30 days	Mon 11/30/09	Fri 1/8/10																			
25	FFE Bid	15 days	Mon 1/11/10	Fri 1/29/10	24																		
26	FFE College Review	15 days	Mon 2/1/10	Fri 2/19/10	25																		
27	FFE Manufactured	65 days	Wed 4/7/10	Tue 7/6/10	26																		
28	FFE Installed	10 days	Mon 7/26/10	Fri 8/6/10	22,27																		
29	AV/IT Programming & Selector	20 days	Mon 11/30/09	Fri 12/25/09																			
30	AV/IT Bid & Advertisement	20 days	Mon 12/28/09	Fri 1/22/10	29																		
31	AV/IT Ordered & Received	30 days	Mon 4/12/10	Fri 5/21/10	30																		
32	AV/IT Installed	15 days	Mon 5/24/10	Fri 6/11/10	31																		
33	COD Occupancy	1 day	Mon 8/9/10	Mon 8/9/10	28																		


Project: PSA Parking & Magnesia Fall: Date: Thu 10/1/09	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	



Project: PSA Parking & Magnesia Fall: Date: Thu 10/1/09	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	




Project: PSA Parking & Magnesia Fall: Date: Thu 10/1/09	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 

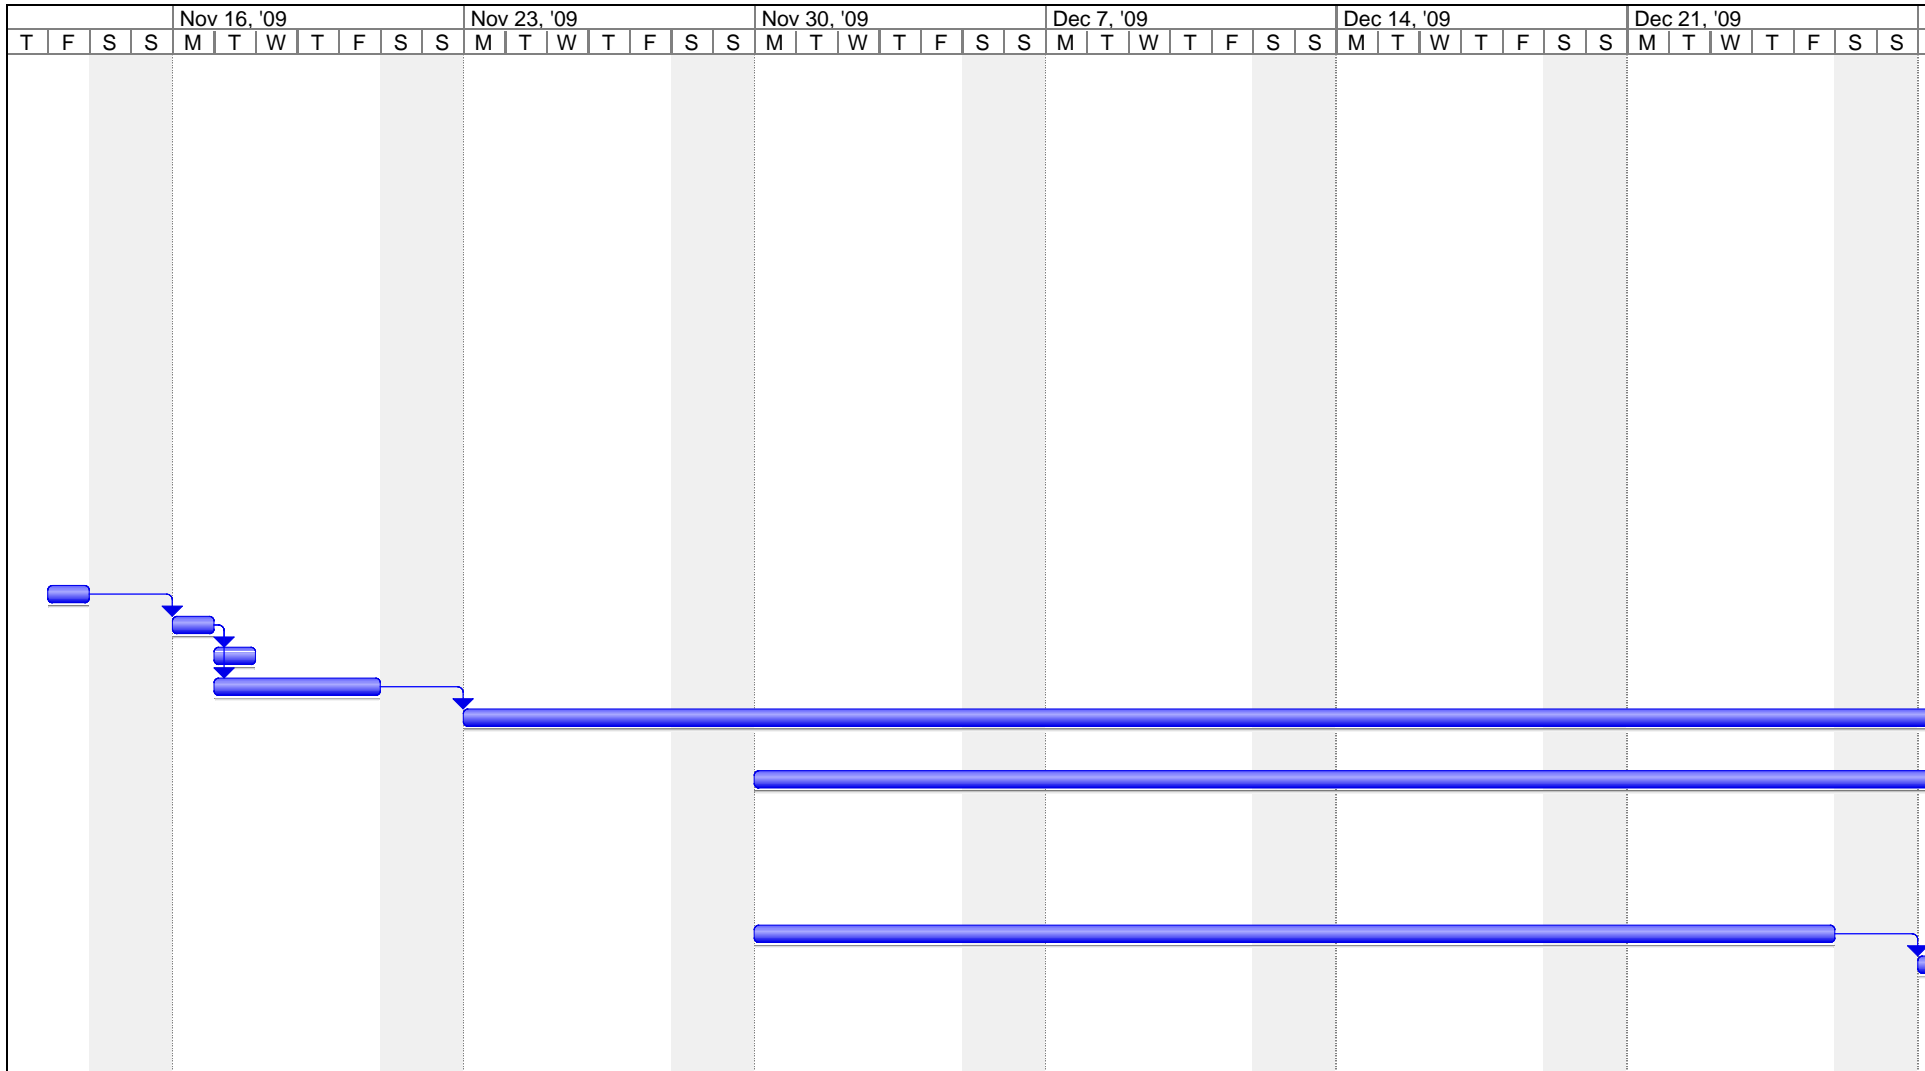


Project: PSA Parking & Magnesia Fall:
Date: Thu 10/1/09

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

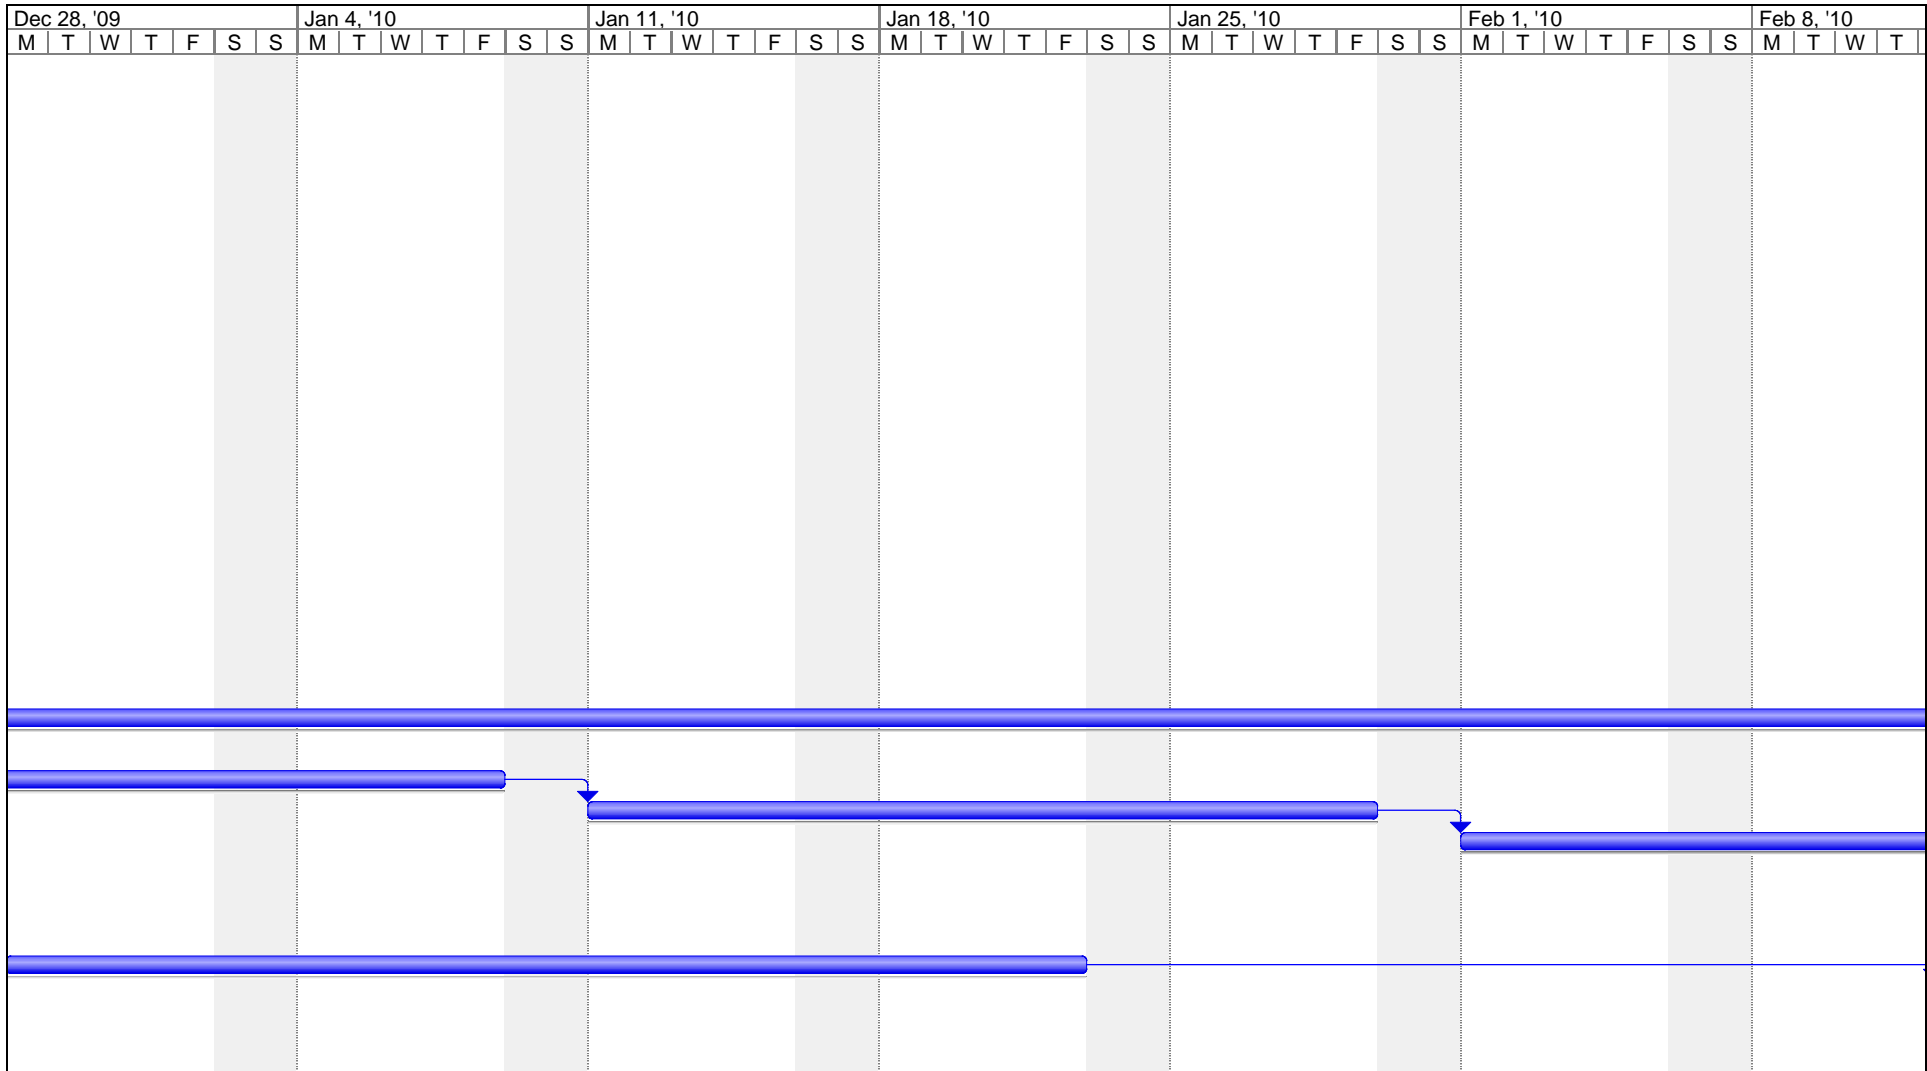





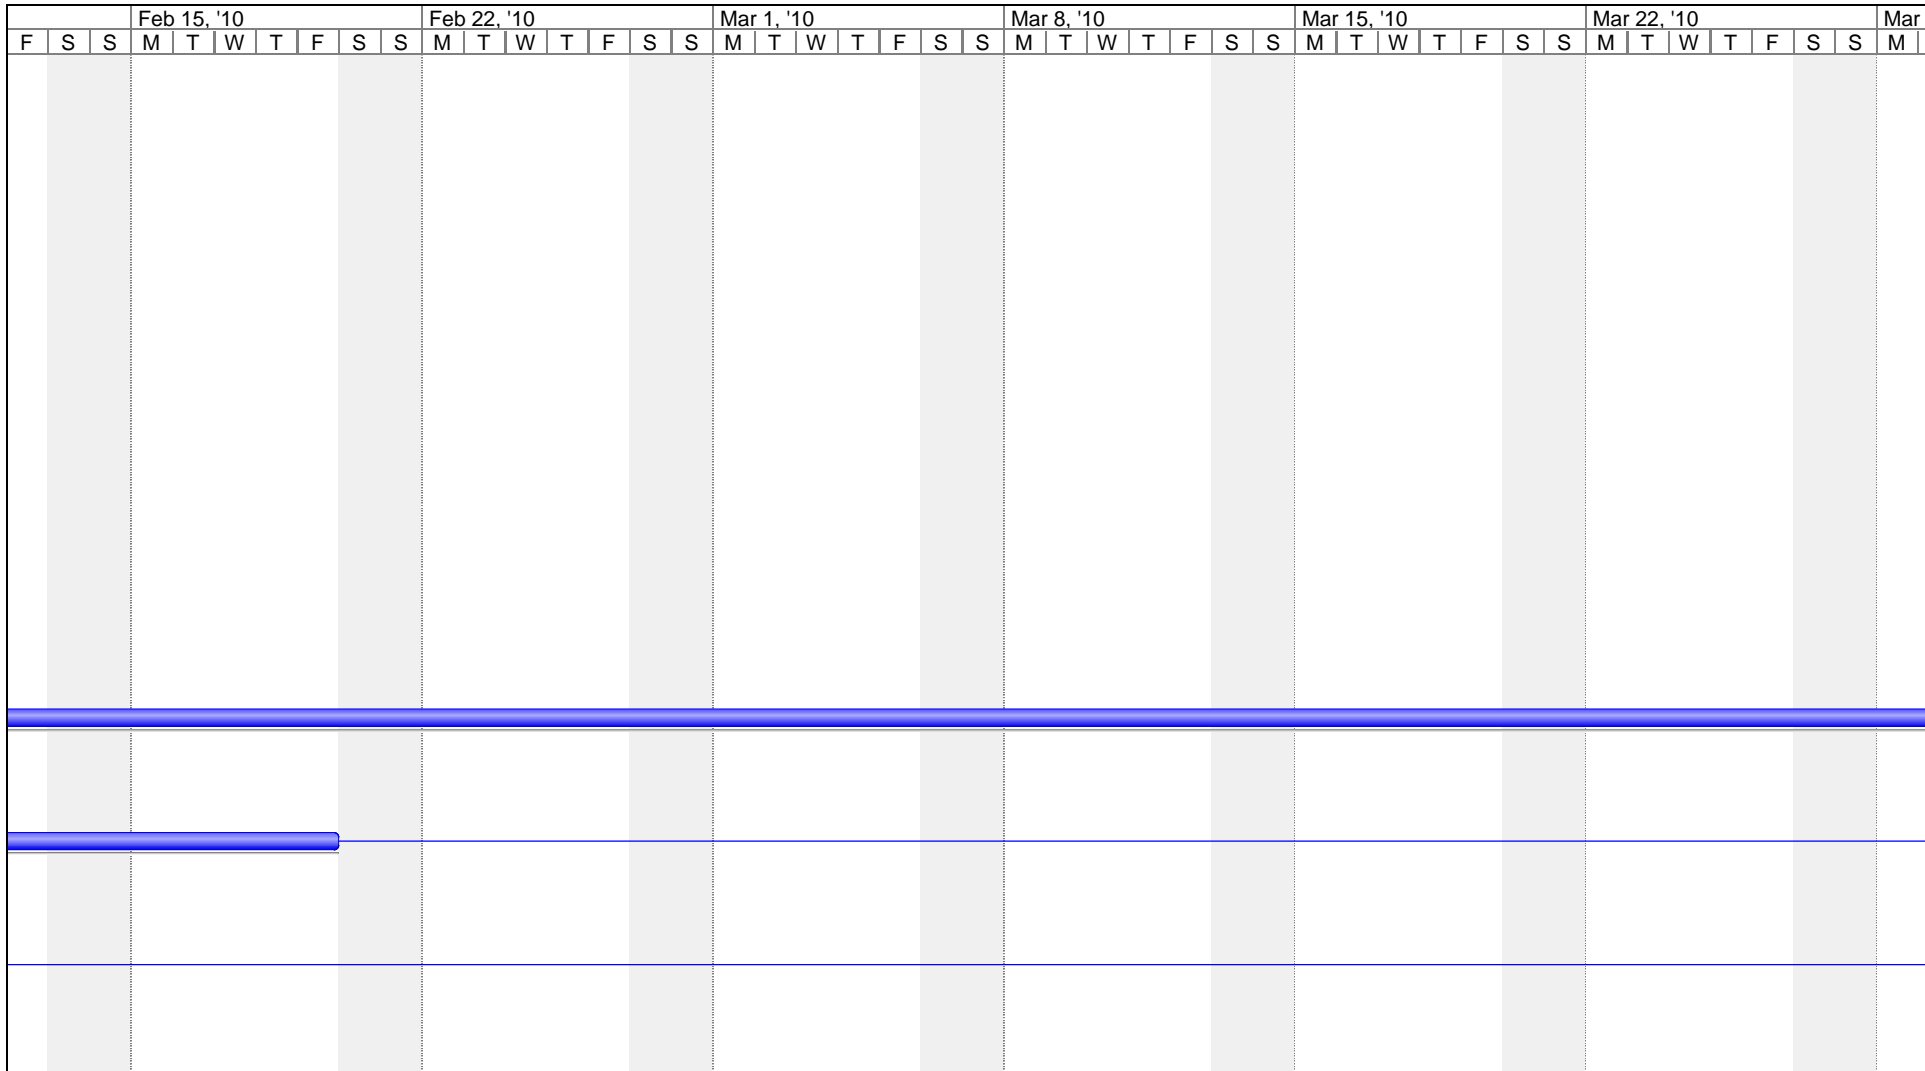

Project: PSA Parking & Magnesia Fall:
Date: Thu 10/1/09

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	




Project: PSA Parking & Magnesia Fall:
Date: Thu 10/1/09


- Task 
- Split 
- Progress 

- Milestone 
- Summary 
- Project Summary 

- External Tasks 
- External Milestone 
- Deadline 

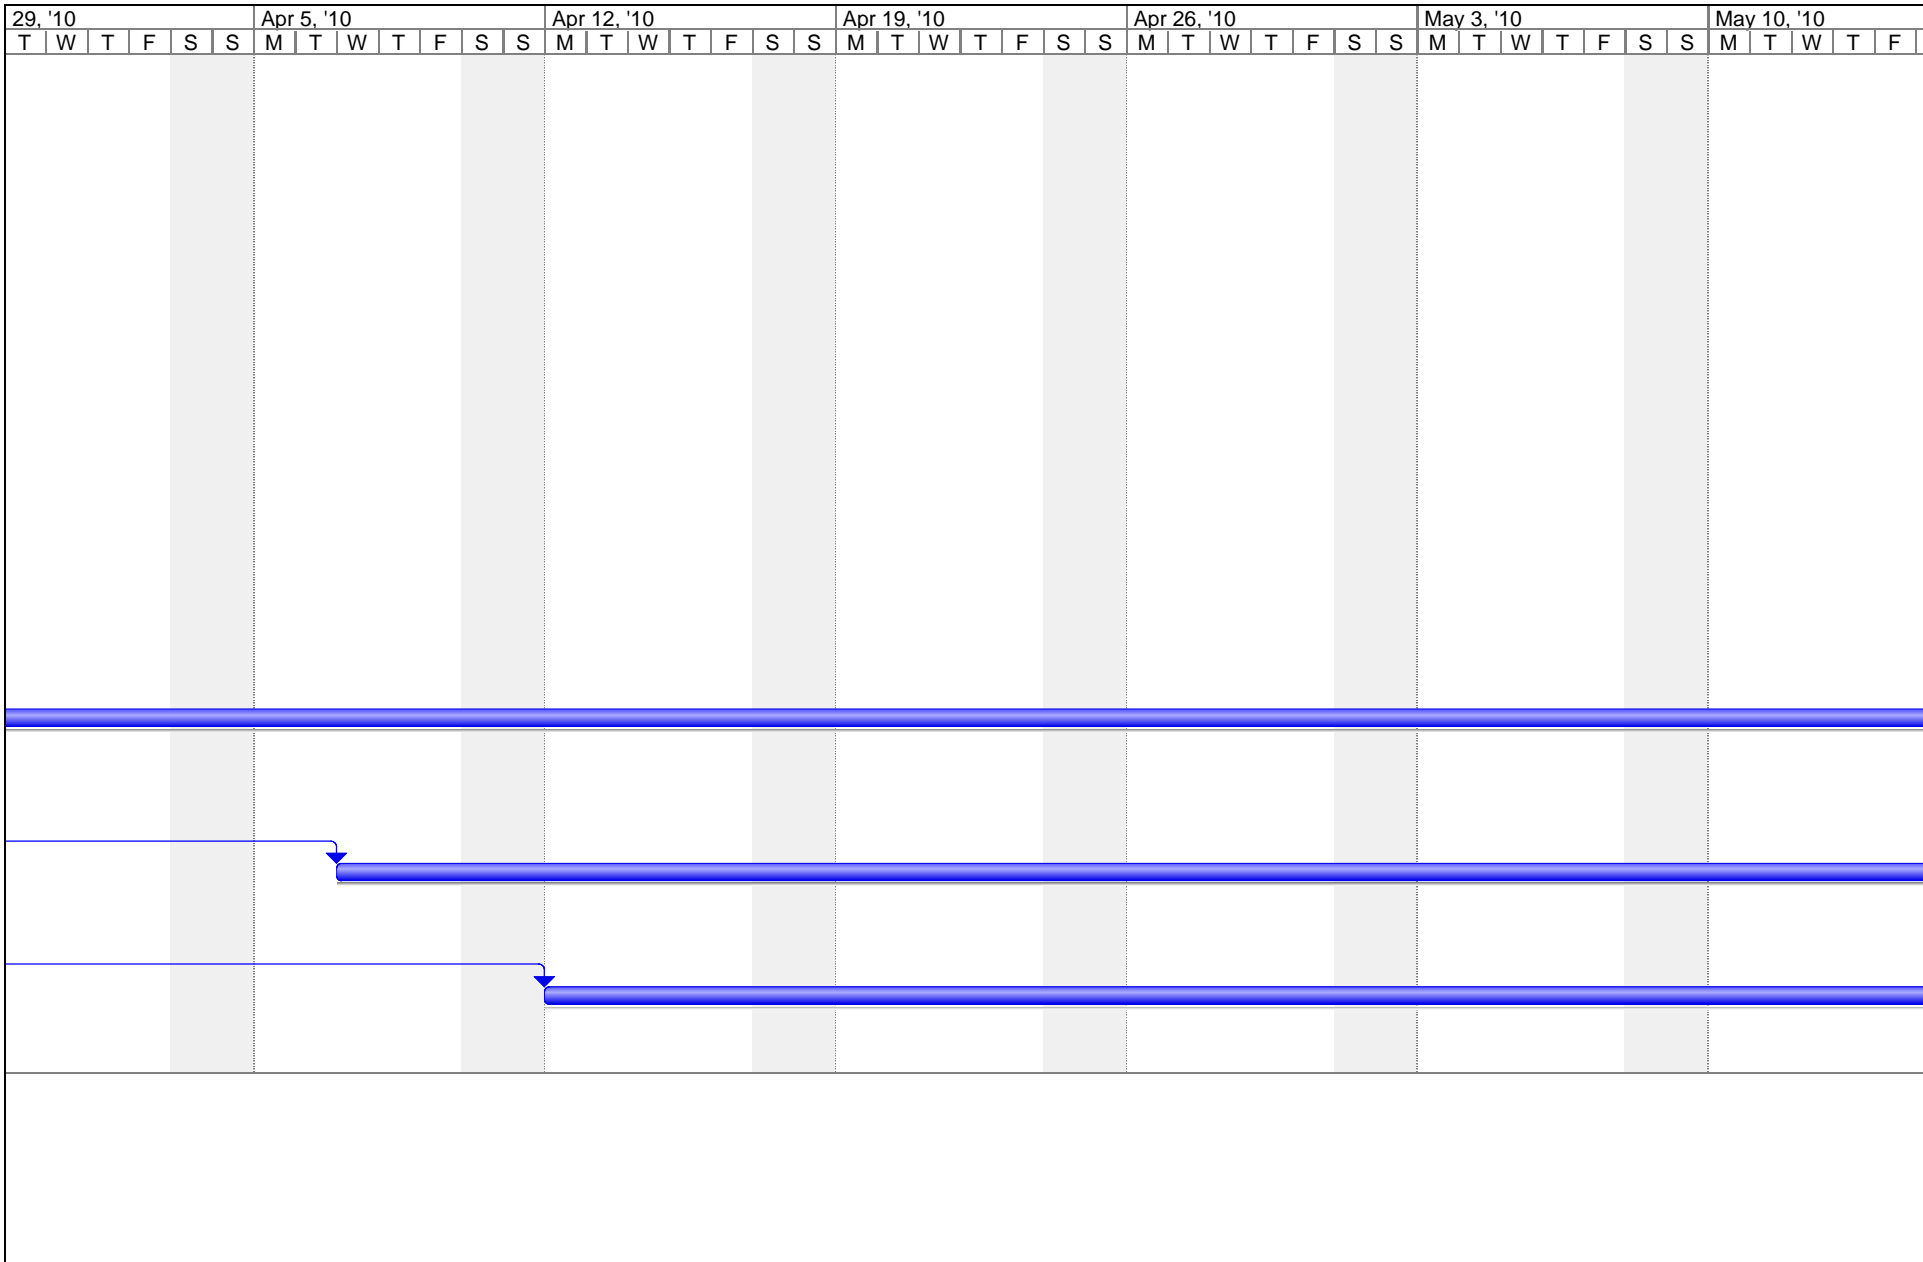


Project: PSA Parking & Magnesia Fall: Date: Thu 10/1/09	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

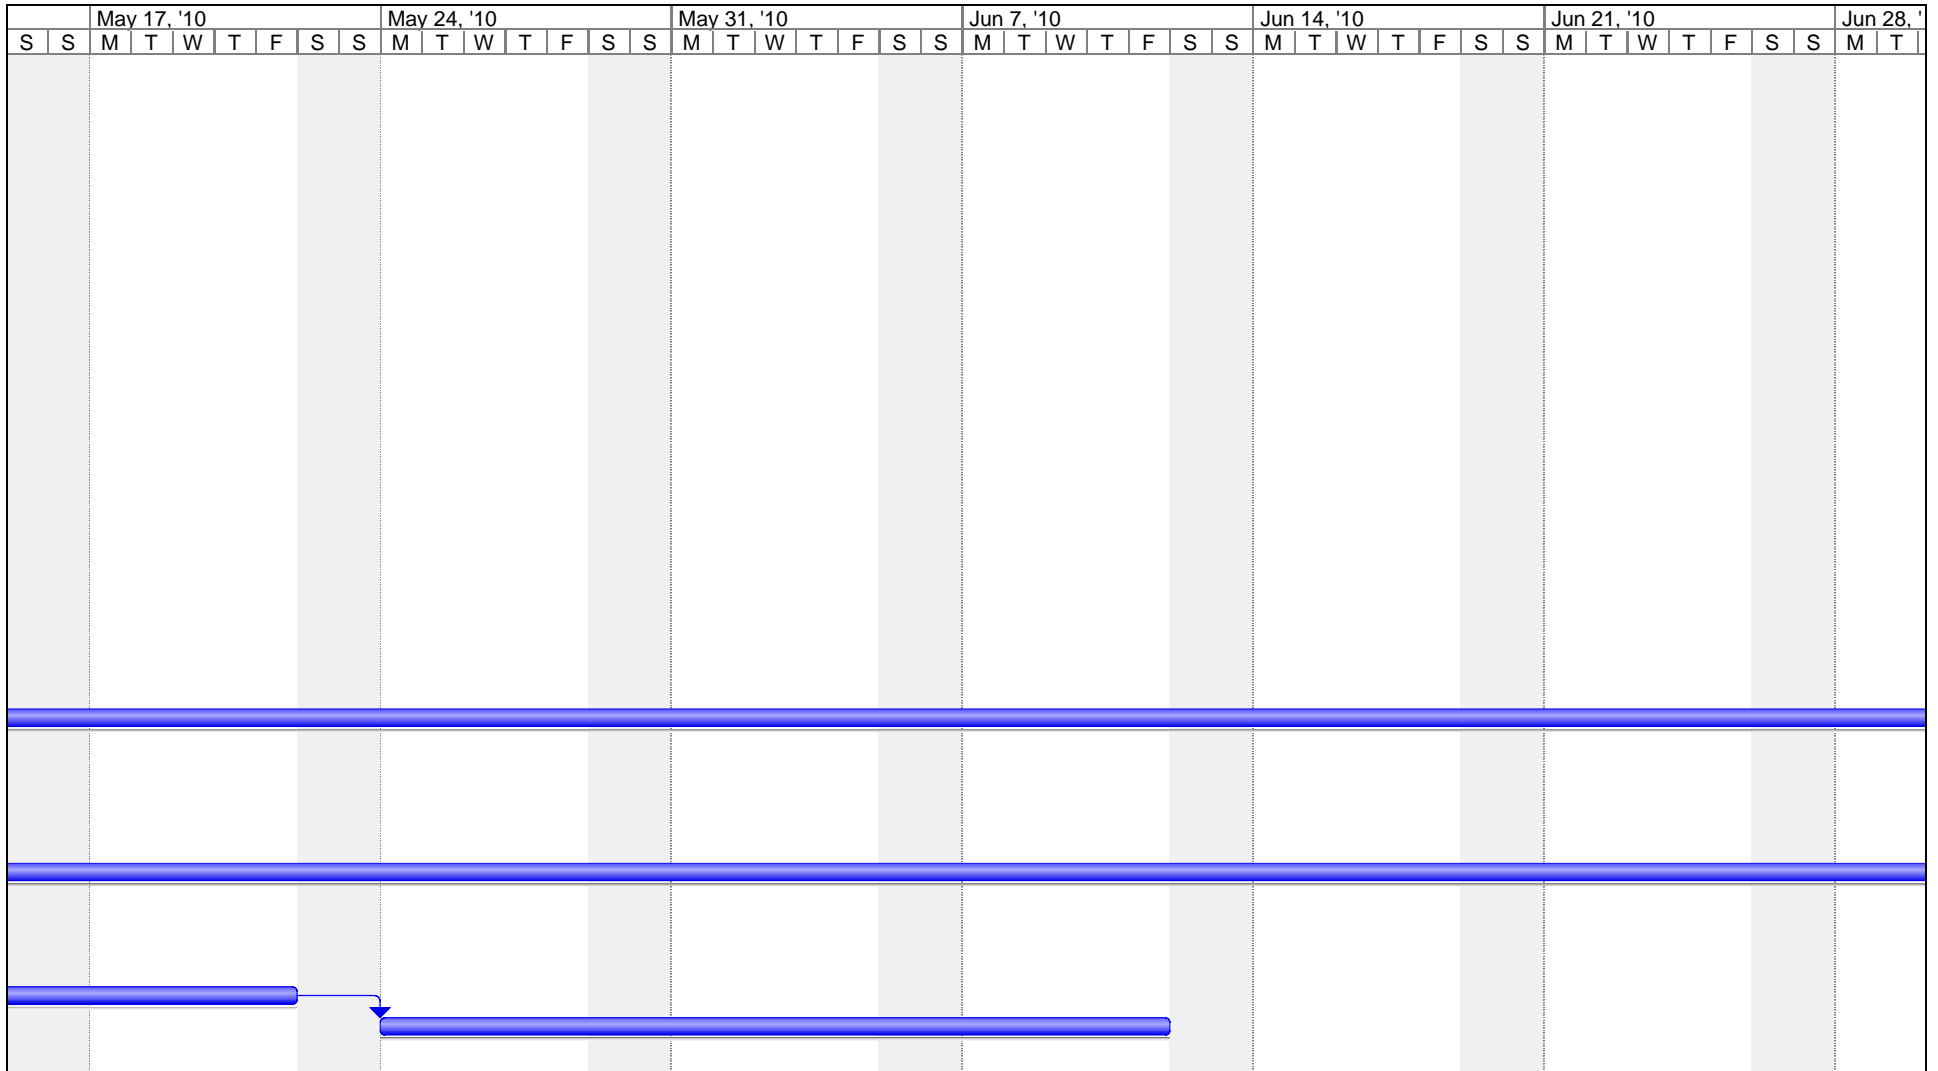





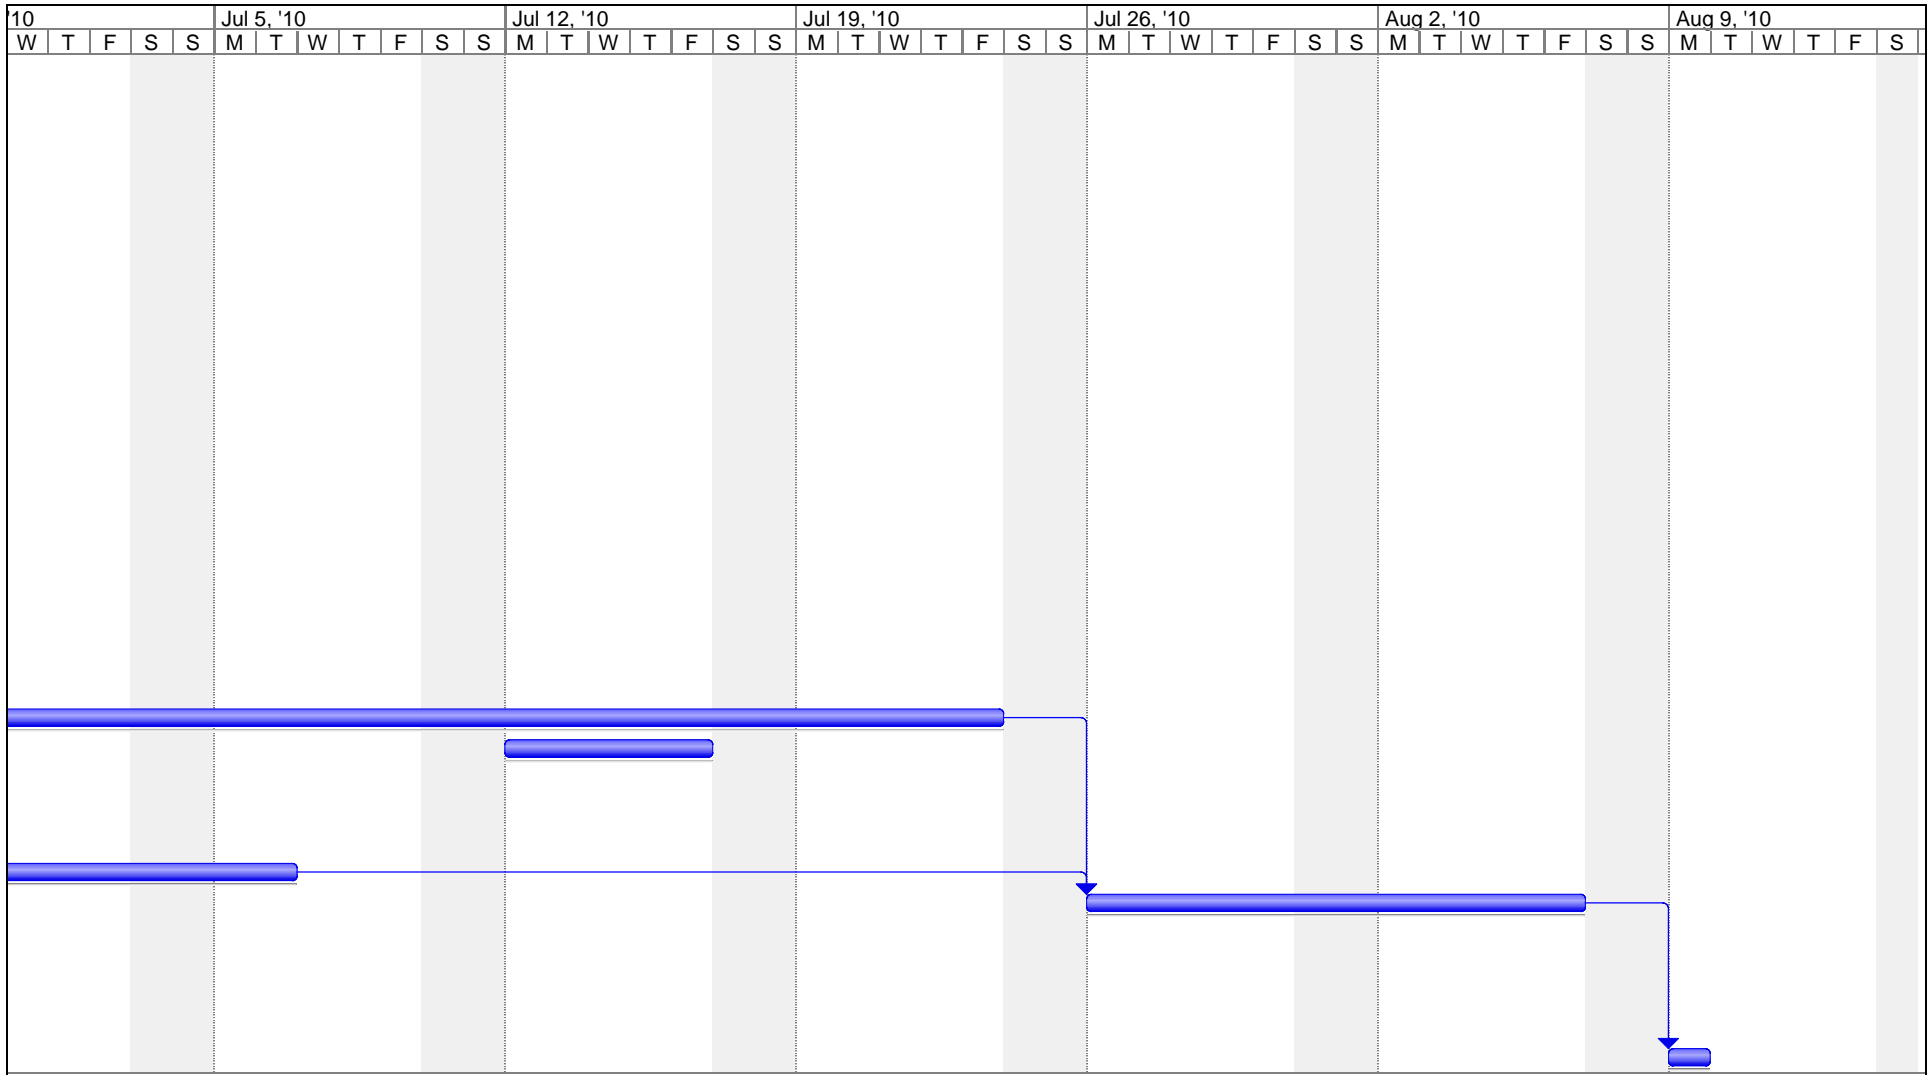



Project: PSA Parking & Magnesia Fall:
Date: Thu 10/1/09

- Task Milestone
- Split Summary
- Progress Project Summary
- External Tasks
- External Milestone
- Deadline



Project: PSA Parking & Magnesia Fall:
Date: Thu 10/1/09

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
